

DPV2 500 kV Transmission Project

Status Report

STEP Informational Item


September 21, 2006




Revised DPV2 Plan of Service

- Eastern Termination at Harquahala Jct
 - Change eastern termination point from Harquahala Generating Station to a new 500 kV Harquahala Jct Switching Substation.
 - Approved by WECC/WATS in June 2005
- West of Devers (WOD)
 - Replace 230 kV upgrades with a new Devers-Valley 500 kV line.
 - Approved by WECC/WATS in June 2006
- Approved by CAISO in September 2006

Revised Eastern Termination

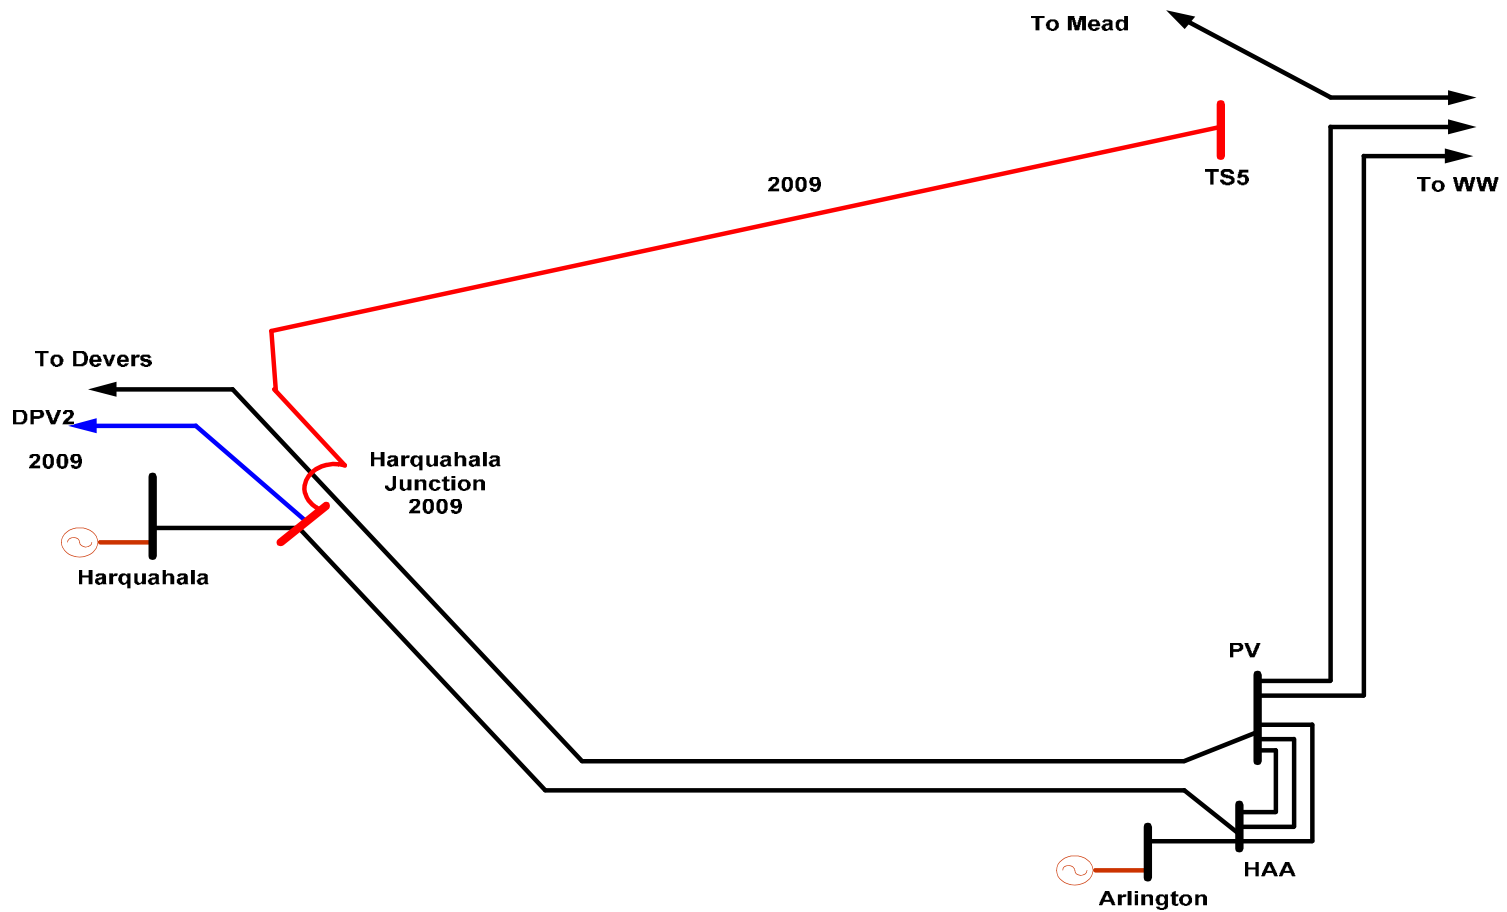

Revised West of Devers

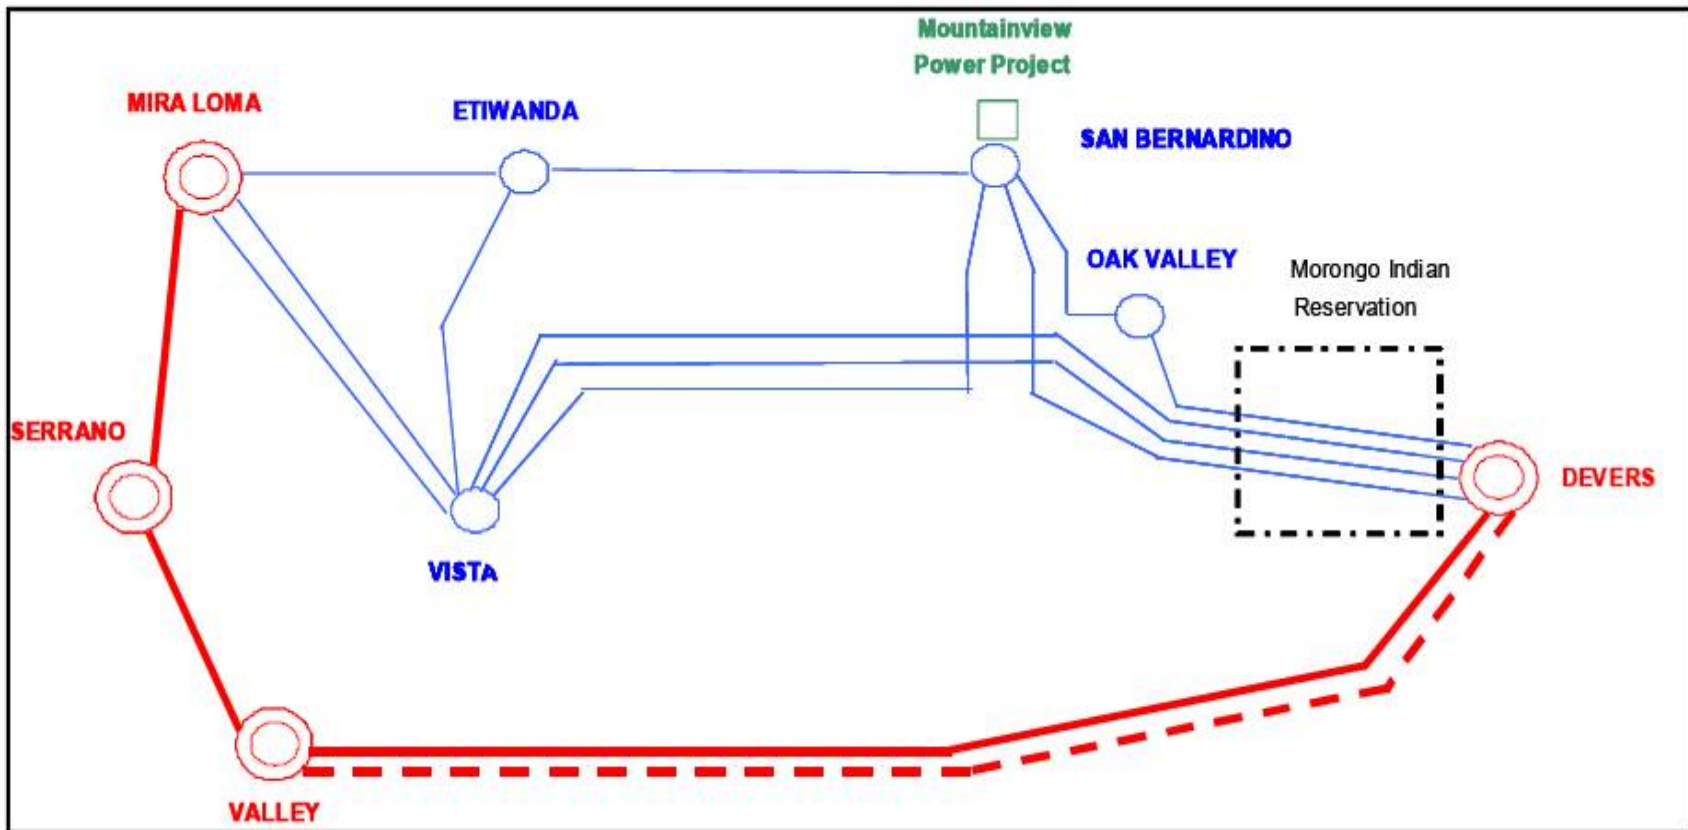



Remaining Studies

- SPS Arming Study (DPV1 and DPV2 Outage)
 - WECC/WATS approved Study Scope and Base Cases in September 2006
 - Target completion date in December 2006
- Combined DPV2/EOR9300 EOR Rating Study
 - Non-simultaneous analysis completed
 - Simultaneous analyses on going
 - Next WECC/WATS meeting scheduled for October 17
 - Target completion date in December 2006
