



Ten West Link 500 kV transmission line and Cielo Azul 500 kV Switchyard

January 29, 2024

CONFIDENTIAL




Project Details

- Ten West Link 500 kV transmission line
 - Project Sponsor – DCR Transmission, L.L.C.
 - Project Awarded – July 2015
 - Project Capacity – 3,200 MW Conductor Capability and 2400 MW Series Compensation Station
 - Line length - 125 miles (103.5 in Arizona and 21.5 miles in California), series compensated line
 - Arizona Terminus – Delaney Substation 500 kV bus (APS)
 - California Terminus – Colorado River 500 kV bus (SCE)
 - Construction Details
 - ✓ Construction Started – October 2022
 - ✓ Construction Completed – February 7, 2024
 - ✓ Expected COD – May 15, 2024
- Cielo Azul Switchyard - A 500 kV, six-bay, 18 breaker, breaker-and-a-half switchyard being constructed to interconnect generation projects submitted in the CAISO LGIP
 - Located approximately 39 circuit miles from Delaney substation
 - Construction commenced early July 2023, anticipated interconnection to Ten West Link date in Q3 2024, Expected COD with Phase 1 of the Project – December 15, 2024




Project Route for Ten West Link and location of Cielo Azul

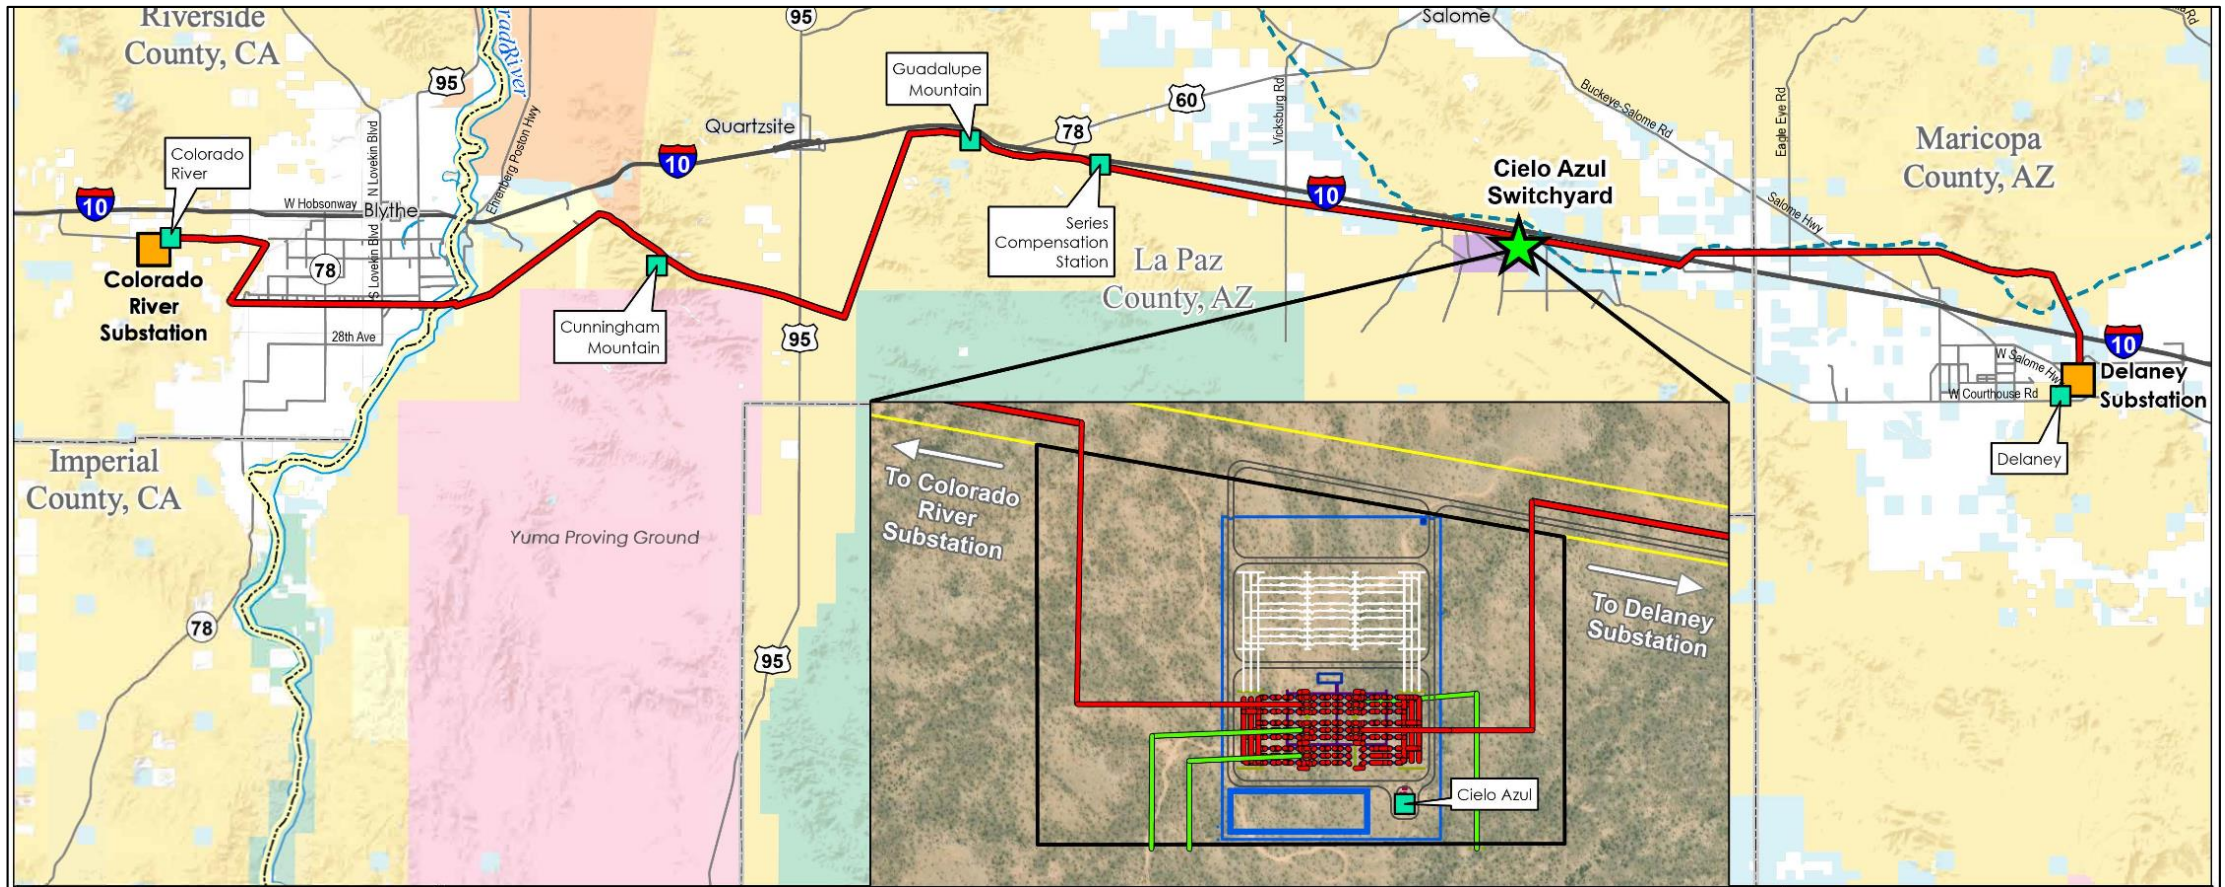



Ten West Link Construction Status

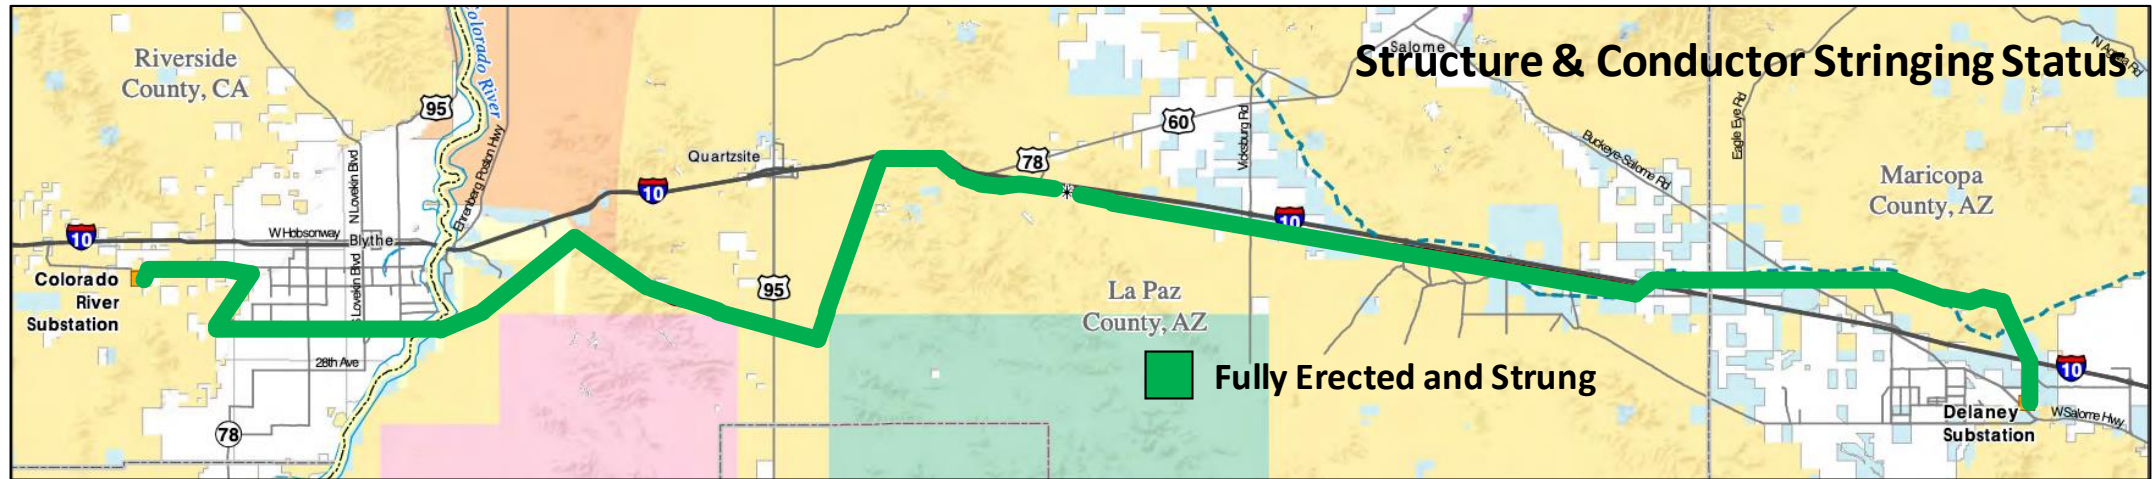

- ✓ Access Roads: 100% complete
- ✓ Foundations: 100% complete
- ✓ Structure Assembly: 100% complete
- ✓ Structure Erection: 100% complete
- ✓ Conductor: 100%+ complete

On Track to achieve Mechanical Completion February 2024





Ten West Link Project location and ground breaking

Project Map

Construction (October 2022)



Illustrative Layout

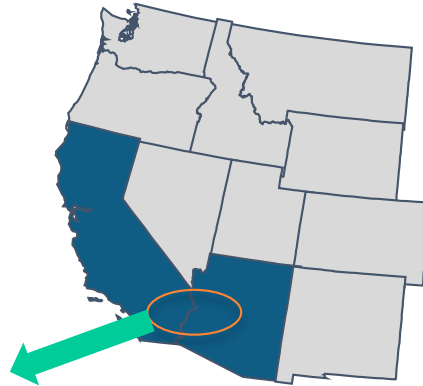

- Substation
- Transmission Line
- Interstate

Groundbreaking



From left to right: AZ governor Harris, CAISO CEO Mainzer, Lotus CEO Saxena, VP Kamala Harris, Interior Secretary Haaland, Energy Secretary Granholm, WH advisor Zaidi



Construction Meeting





Helicopter Construction through Copper Bottom Pass



DIRECTION
258 deg(T)

33.60493°N
114.38809°W

ACCURACY 5 m
DATUM WGS84

Structure 306

Flying out Arm's for
Erection.

2023-11-03
11:38:55-07:00



Series Compensation Station





Cielo Azul Switchyard



Groundbreaking in August...grading complete and fence being installed.

