


# **Intermountain Power Project Southern Transmission System Upgrade from 1920 MW to 2400 MW**

Presentation to  
Southwest Transmission Expansion Planning

March 16, 2007  
San Diego, California

by  
Tim Wu  
Los Angeles Department of Water & Power

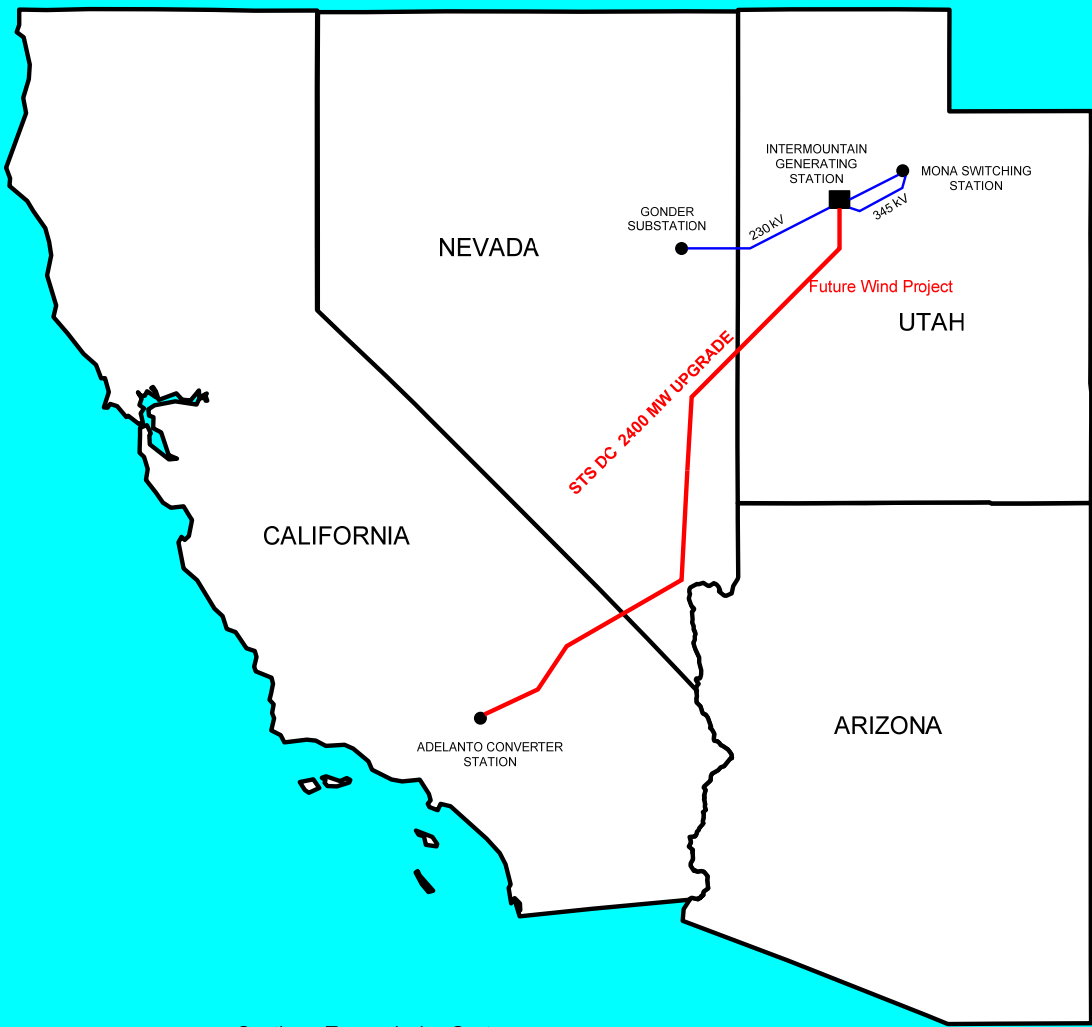

— Southern Transmission System  
— Northern Transmission System

# WECC Rating Study Progress

- Achieved WECC Phase II on November 9, 2006
- WECC Project Review Group meetings on 12-12-06 and 2-20-07
- WECC PRG approved Phase 2 Study Plan on 1-23-07
- WECC PRG approved simultaneous results on 2-20-07 on TOT2B/C, Path 26, and Path 61.

# Remaining Works

- Simultaneous with Path 41,46, 32 and SCIT

# Milestones

- Presentation to STEP 07/2006
- Comprehensive Progress Report 08/23/2006
- Phase II 11/09/2006
- STEP presentation 11/17/2006
- Project Review Group meeting 12/12/2006  
and 2/20/07
- Complete WECC Path Rating Studies 05/2007
- Start Construction 12/2007
- Complete Construction 03/2008
- Commission & Operation 04/2008
