



















ID	Task Name	Duration	Q3 '08			Q4 '08			Q1 '09			Q2 '09	
			Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May
1	Participating Load (R1)	180 days?		█	█	█	█	█	█	█	█	█	█
2	Kickoff	1 day?											
3	CAISO Process & Requirements	180 days?		█	█	█	█	█	█	█	█	█	█
4	Business Process Development	55 days		█	█	█	█						
8	Contracts	30 days		█	█	█							
11	Resource Registration	27 days		█	█	█							
15	Metering	5 days			█	█							
18	Telemetry (A/S Only)	180 days		█	█	█	█	█	█	█	█	█	█
24	PL Implementation Plan	1 day?		█									
28													
29	LSE Business Activities	1 day?		█									
30													
31	DR Pilot Planning / Design	1 day?		█									
36	DR Customer Enrollment	1 day?		█									
39	Capability Development	1 day?		█									
43	Testing	1 day?		█									
46	Certification, Final Tuning and Rollout	1 day?		█									
50	On-going Operations	1 day?		█									
51	DR Pilot Administration	1 day?		█									
55	Pilot Operation	1 day?		█									
59	Pilot Program Reporting	1 day?		█									
62													
63	Curtailment Service Provider Business Activities	1 day?		█									
65													
66													
67	CPUC Regulatory Process	1 day?		█									
68	Program/Tariff Development	1 day?											
69	Program/Tariff Approval	1 day?											
70													
71	Proxy Demand Resource	697 days?											█

Project: Project1 Date: Tue 8/19/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	










ID	Task Name	Duration	Q3 '08			Q4 '08			Q1 '09			Q2 '09	
			Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May
72	kickoff	1 day?											
73	CAISO Process & Requirements	200 days?											
74	Stakeholder Process	1 day?											
75	Business Process Development	1 day?											
77	Tariff Review	1 day?											
78	Contracts	1 day?											
79	Resource Registration	11 days?											
80	Metering for Extended PDR	1 day?											
81	Telemetry (A/S Only)	1 day?											
82	Market Simulation Support	1 day?											
83													
84	IOU Business Activities	1 day?											
97													
98	Regulatory Process	1 day?											
101													
102	End Date	1 day?											
103													
104	Participating Load/DDR (MAP)	436 days?											
105	Kickoff	1 day?											
106													
107	CAISO Process & Requirements	180 days?											
108	Business Process Development	1 day?											
112	Contracts	30 days											
115	Resource Registration	27 days											
119	Metering	5 days											
122	Telemetry (A/S Only)	180 days											
128	PL Implementation Plan	1 day?											
130													
131	IOU Business Functions	1 day?											
132	Customer Services	1 day?											

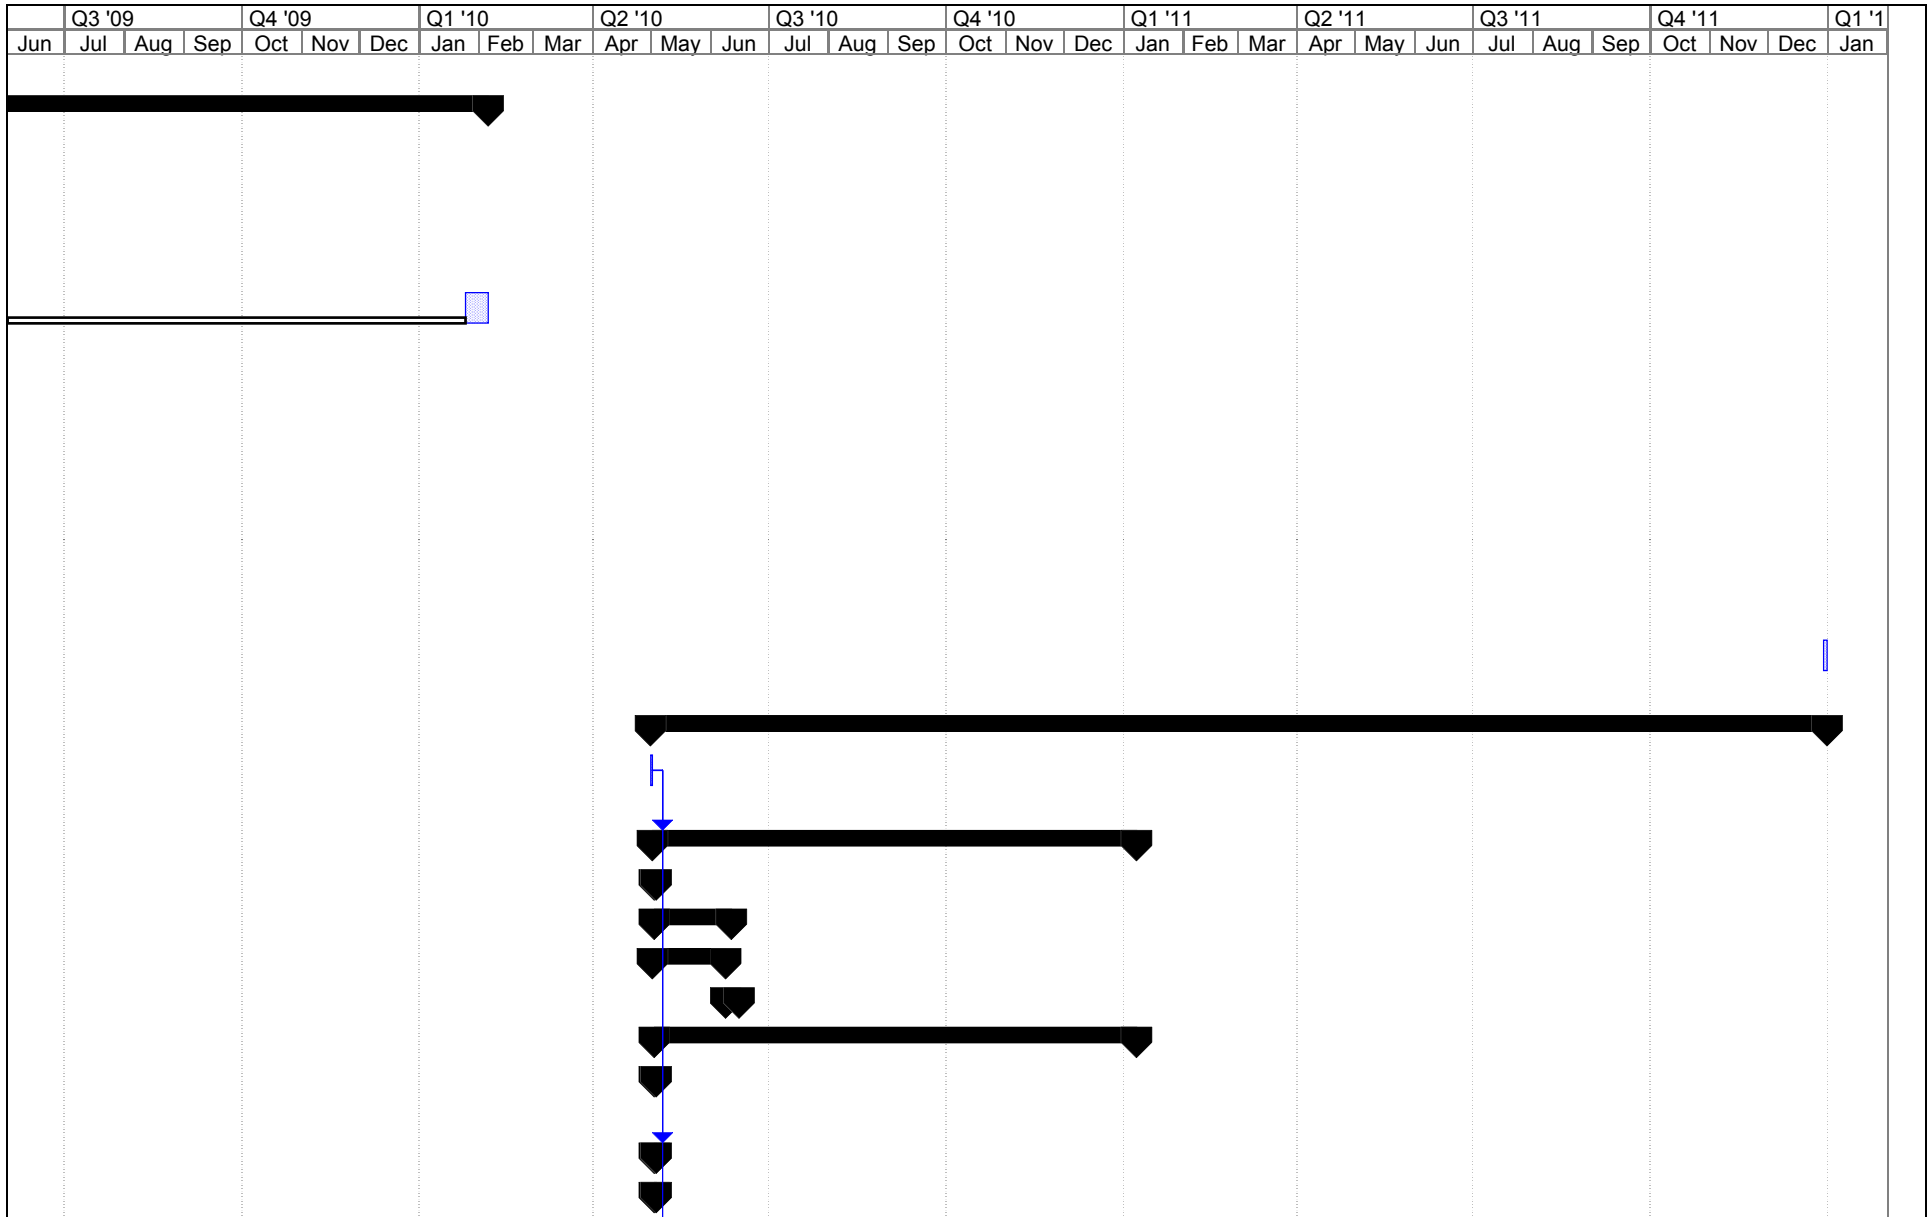
Project: Project1 Date: Tue 8/19/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

ID	Task Name	Duration	Q3 '08			Q4 '08			Q1 '09			Q2 '09	
			Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May
135	Power Marketing	1 day?											
138	System Operations	1 day?											
140	Information Technology	1 day?											
143													
144	<u>Regulatory Process</u>	1 day?											
147													
158	End Date	1 day?											





Project: Project1 Date: Tue 8/19/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

	Q3 '09				Q4 '09			Q1 '10			Q2 '10			Q3 '10			Q4 '10			Q1 '11			Q2 '11			Q3 '11			Q4 '11			Q1 '11
Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	









Project: Project1 Date: Tue 8/19/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	



Project: Project1 Date: Tue 8/19/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

Q3 '09				Q4 '09			Q1 '10			Q2 '10			Q3 '10			Q4 '10			Q1 '11			Q2 '11			Q3 '11			Q4 '11			Q1 '11				
Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan				
										   																									



Project: Project1 Date: Tue 8/19/08	Task 	Milestone 	External Tasks 
	Split 	Summary 	External Milestone 
	Progress 	Project Summary 	Deadline 
