

MICHAEL KUNSELMAN PHONE 202.295,8465 FAX 202.424,7643 MNKUNSELMAN@SWIDLAW.COM THE WASHINGTON HARBOUR 3000 K STREET, NW, SUITE 300 WASHINGTON, DC 20007-5116 PHONE 202.424.7500 FAX 202.424.7647

WWW.SWIDLAW.COM

January 10, 2005

The Honorable Magalie R. Salas Secretary Federal Energy Regulatory Commission 888 First Street, N.E. Washington, D.C. 20426

Re: California Independent System Operator Corporation Docket Nos. ER03-746-000, et al.
San Diego Gas & Electric Co., et al.
Docket Nos. EL00-95-081, et al.

Dear Secretary Salas:

Enclosed please find one original and fourteen copies of the Twelfth Status Report of the California Independent System Operator Corporation on Re-Run Activity filed in the above-captioned dockets.

Also enclosed are two extra copies of this cover letter to be time/date stamped and returned to us by the messenger. Thank you for your assistance. Please contact the undersigned if you have any questions regarding this filing.

Sincerely

Michael Kunselmar

Counsel for the California Independent System Operator Corporation

Enclosures

UNITED STATES OF AMERICA BEFORE THE FEDERAL ENERGY REGULATORY COMMISSION

California Independent System Operator Corporation) Docket No.))	ER03-746-000
San Diego Gas & Electric Company, Complainant,)))	
v .) Docket Nos.	EL00-95-081 EL00-95-074
Sellers of Energy and Ancillary Services Into Markets Operated by the California Independent System Operator and the California Power Exchange, Respondents.	,))))	EL00-95-086
Investigation of Practices of the California Independent System Operator and the California Power Exchange) Docket Nos.)	EL00-98-069 EL00-98-062 EL00-98-073
	, , ,	:* # <i>e</i> #\

(not consolidated)

TWELFTH STATUS REPORT OF THE CALIFORNIA INDEPENDENT SYSTEM OPERATOR CORPORATION ON SETTLEMENT RE-RUN ACTIVITY

Pursuant to the Order Granting Clarification and Granting and Denying Rehearing of the Federal Energy Regulatory Commission ("Commission" or "FERC"), issued on February 3, 2004, in the above captioned dockets ("February 3 Order"), the California Independent System Operator Corporation ("ISO") hereby provides its twelfth regular monthly status report.¹

The Commission's Order at paragraph 21 states, "The CAISO is hereby directed to submit to the Commission on a monthly basis, beginning on February 10, 2004, a report detailing the status of the preparatory adjustment re-runs and the dates that it expects to complete both the preparatory re-runs and the settlement and billing process for calculating refunds, as discussed in the body of this order." 106 FERC \P 61,099 (2004).

I. BACKGROUND²

On April 15, 2003, the ISO³ filed Amendment No. 51 to its Tariff, to which the Commission assigned Docket No. ER03-746 ("Amendment No. 51 filing"). In the Amendment No. 51 filing, the ISO proposed to conduct a preparatory re-run in preparation for the Commission-mandated re-run in the California refund proceeding (Docket Nos. EL00-95-045, *et al.*) and requested approval of Tariff amendments to "wall off" that re-run from the settlement processes currently in use to clear the ISO Market.

On December 15, 2003, the ISO filed its request for rehearing of the Commission's November 14 order in Docket No. ER03-746. Therein, the ISO informed the Commission that it could not provide the ordered compliance filing by January 30th, but instead would make the filing as soon as practicable. In the February 3 Order, the Commission granted the ISO the additional time needed to make the compliance filing for the preparatory re-run, but also required the ISO "to submit to the Commission on a monthly basis, beginning on February 10, 2004, a report detailing the status of the preparatory adjustment re-runs and the dates that it expects to complete both the preparatory re-runs and the settlements and billing process for calculating refunds." February 3 Order at P

In its October 16, 2003 Order on Rehearing, 105 FERC ¶ 61,066 (2003) the Commission ordered the ISO to file within five months of the date of the order the results of the preparatory reruns along with the appropriate explanations. The ISO considers that this directive has been overtaken by FERC's later recognition in the Amendment 51 proceeding that the ISO could not possibly comply with the deadline in the October 16 Rehearing order, as well as the deadlines in the previous Amendment 51 orders. The ISO is endeavoring to comply, however, with FERC's directive that the ISO work as fast as practicable, keep the parties well informed, and file monthly status reports. For this reason, in addition to the Amendment No. 51 docket, the ISO is also filing this report in the dockets associated with the California refund proceeding.

³ Capitalized terms not otherwise defined herein shall have the meanings set forth in the Master Definitions Supplement, Appendix A to the ISO Tariff.

21. The first such status report was filed with the Commission on February 9, 2004. This filing constitutes the twelfth such report required by that Commission Order. While the preparatory re-run is complete, the ISO will continue to provide monthly status reports throughout the refund re-run because the ISO believes that these reports have been a valuable tool for communicating with the Commission and Market Participants, in addition to meeting the Commission-mandated reporting requirement.

II. CURRENT STATUS OF RE-RUN ACTIVITY

The refund re-run settlement statement publishing began on October 27, 2004. This work utilizes the MMCPs which were previously calculated and published to Market Participants along with the transactional data from the preparatory re-run. The publishing activity went on hold November 19th due primarily to the increased activity associated with settlements of a new market design, the Phase 1B implementation of MRTU. As of November 19, 2004, the ISO had published re-run statements through February 2, 2001.

Re-run production was restarted January 5, 2005. At the current production rate, publishing of re-run statements will be completed mid-February, 2005. This was communicated via market notice on January 4, 2005 which gave notice of the re-start and the projected completion date of this phase of the work activity (Mid February 2005). The ISO's notice went on to state that it will publish several manual re-run corrections on January 5, 2005 to adjustments made previously as a part of this re-run process. The largest of the manual adjustment issues relates to generators that were paid over the bid cap and were

inadvertently not mitigated. A number of the other corrections were related to individual billing inquiries submitted by various parties.

In response to several questions from Market Participants the ISO posted on its website in the FERC refund re-run section⁴, a description of the method that it plans to use to mitigate import transactions on the interties. In addition to the description, the ISO has included a series of transactional examples in its posting.

The ISO again wishes to note that although the Commission's November 23, 2004 Order on Rehearing⁵ in this proceeding resolved many of the "open issues," it did not address the matter of the ISO compliance filing in Tariff Amendment 41 which would require the recalculation of interest for the refund period. A decision on this pending amendment and the ISO's associated request for rehearing may allow the ISO to distribute as much as \$6 million to the ISO Market that is currently being held in escrow pending the Commission's decision.

The ISO has continued to interface with Market Participants via market notices, telephonic conferences, and direct consultation, as necessary.

Specifically, the ISO held its most recent regular monthly telephonic meeting with Market Participants to discuss re-run issues on Wednesday, December 1st. The ISO has posted on its web site, and continues to update, a calendar containing

⁵ 109 FERC ¶ 61,218 (2004)

4

⁴ http://www.caiso.com/docs/2005/01/03/2005010308312727756.pdf

the schedule for the re-run activity, and has provided the link to that calendar in a market notice.⁶

As of January 6, 2005, the ISO has received a total of 26 billing inquiries from Market Participants with respect to questions related to the Refund re-run statements. Twenty- three of the 26 inquiries have been answered by the ISO's Market Quality department and returned to the respective Market Participant. The remaining 3 inquiries are still under investigation.

Upcoming Stakeholder communications will include the regular monthly call with Market Participants scheduled for later in the week of January 10, 2005.

III. ESTIMATED SCHEDULE FOR COMPLETION OF THE REFUND RE-RUN ACTIVITY

Attachment A to this status report contains the ISO's current estimate of the final completion date for the FERC refund re-run phase of the project. As noted above, the preparatory re-run was completed July 16th. Note that the compliance filing after the refund re-run will include adjustments for fuel price, emissions and interest, but will not include adjustments for the various global settlements. This schedule is consistent with the Commission's order of November 23, 2004 and with the discussions held with Market Participants and Commission staff on July 26th in Washington, as well as the ISO's presentation at the technical conference on October 7th.

The ISO's re-run calendar, market notices, and re-run procedure manual are located on the ISO's website at http://www.caiso.com/docs/2004/10/26/2004102612304417309.xis (Update link to Refund re-run)

IV. CONCLUSION

The ISO respectfully requests that the Commission accept the ISO's twelfth status report in compliance with the Commission's February 3 Order, referenced above.

J. Phillip Jordan Michael Kunselman

Swidler Berlin, LLP 3000 K Street, Ste. 300 Washington, D.C. 20007 Telephone: (202) 424-7500

Counsel for the California Independent System Operator Corporation

Respectfully submitted,

Charles F. Robinson General Counsel Gene L. Waas Regulatory Counsel


The California Independent System Operator Corporation 151 Blue Ravine Road Folsom, CA 95630

Telephone: (916) 608-7049

Dated: January 10, 2005

Attachment A Refund Re-run Project January 10, 2005

NOTE: Current ISO constraints and FCA audit could shift schedule up to 4 weeks

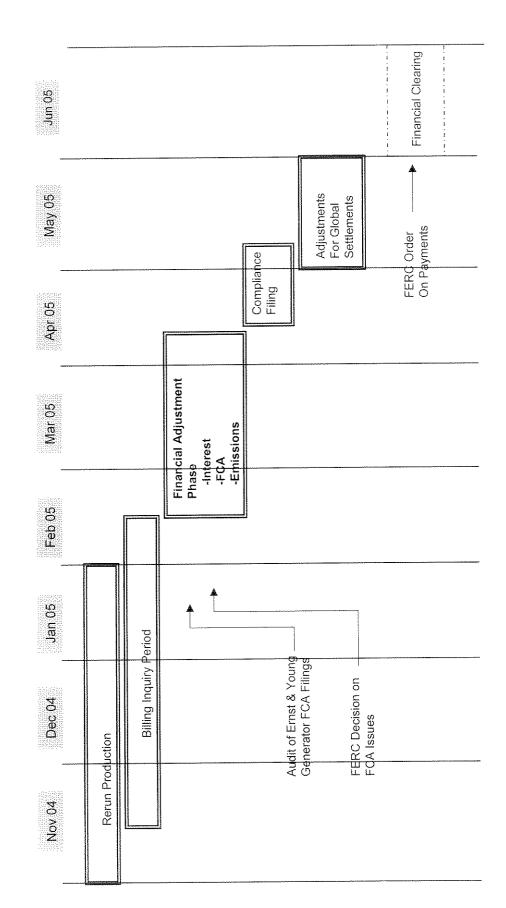

ATTACHMENT A - RE-RUN SCHEDULE

January 10, 2005

Key assumptions/comments to support the schedule (Updated for the refund rerun)

- A schedule revision was presented at the FERC conference on October 7, 2004. October 7th marked the completion of the prep re-run phase including the production of settlement statements, filing by participants and resolution of over 5,000 disputes, and the filing of the compliance report with FERC on October 6, 2004.
- The ISO envisions the following additional phases of the refund project:
 - o Refund rerun settlement statement production this phase began on October 27th. Scheduled for completion in mid February, 2005.
 - o Financial adjustment phase scheduled for approximately 6 weeks following completion of the refund rerun statement production and earlier receipt of:
 - (1) Resolution from FERC of open issues relative to fuel cost allowance
 - (2) Submittal to the ISO of the fuel cost allowances following audit by Ernst and Young
 - The ISO will submit its compliance filing at the end of this phase.
 - Adjustment for global settlements the ISO will make adjustments to invoices based on written instructions from the settling parties.

 These adjustments will affect the owed and owing of the settling parties only and will not affect non-settling parties.
- This schedule assumes that SCs submit billing inquiries during the process and do not hold them until the final deadline for inquiries set for two weeks after the publishing of the June 2001 statements. The ISO will begin work in parallel with the final billing inquiries receipt and resolution.

CERTIFICATE OF SERVICE

I hereby certify that I have this day served the foregoing document upon each person designated on the official service list for the captioned proceeding, in accordance with Rule 2010 of the Commission's Rules of Practice and Procedure (18 C.F.R. § 385.2010).

Dated at Folsom, CA, on this 10th day of January, 2005.

Gene L. Waas
