



Release User Group Agenda

November 5th, 2019

10:00 a.m.–11:00 a.m. (Pacific Time)

Web Conference Information	Conference Call Information
<p>Web Address: https://caiso.webex.com/meet/RUG Meeting Number: 960 941 245</p> <p>Audio connection instructions will be available after connecting to the web conference. When prompted, select "Call me" and enter the phone number you will use during the call. You will be called by the conference shortly.</p>	<p>Dial-in Number: 866-528-2256 International Dial-in: 216-706-7052 Access Code: 291 426 5</p>
<p>Calls and webinars are recorded for stakeholder convenience, allowing those who are unable to attend to listen to the recordings after the meetings. The recordings will be publicly available on the ISO web page for a limited time following the meetings. The recordings, and any related transcriptions, should not be reprinted without the ISO's permission.</p>	

Release User Group Agenda

November 5th, 2019

10:00 a.m. – 11:00 a.m. (Pacific Time)

Time	Topic	Facilitator
10:00 – 10:05	Agenda & ISO Roll call	Adrian Chiosea
10:05 – 10:45	Release Plan	Trang Deluca Cynthia Hinman Christopher McIntosh Jeremy Malekos Janet Morris

The ISO offers innovative training programs

Date	Training courses and workshops
October 29	Existing Day-ahead Market Training (associated with EDAM initiative) – FULL
November 12	Existing Day-Ahead Market Training (associated with EDAM initiative) – FULL
January 9	Welcome to the ISO Webinar
January 28	ISO Workshop - Introduction to ISO Markets (Folsom)
January 29	ISO Workshop - Market Transactions (Folsom)
January 30	ISO Workshop – ISO Settlements (Folsom)



CustomerTraining@caiso.com

New Modules (recorded webinar and slides)

You can find new initiatives training courses on the learning center web page below. More resources will be added throughout 2019/2020 in accordance with project schedules.

Computer Based Training

There are more than 20 computer based training modules on the ISO website covering:

- Markets and Operations
- Reference Materials
- Settlements and Metering
- Western Energy Imbalance Market

Visit our **Learning Center** web page to access our training calendar, register for courses and find other informational resources:

<http://www.caiso.com/participate/Pages/LearningCenter/default.aspx>

Release Plan Summary: 2019

Fall 2019

- Commitment Costs and Default Energy Bid Enhancements Phase 1
- Energy Storage and Distributed Energy Resources Phase 3A
- RMR and CPM Enhancements
- Local Market Power Mitigation Enhancements
- EIM 2019 Enhancements
- FERC Order 841 – Energy Storage Resources
- Real-Time Market Neutrality Settlement

Spring 2020

- Energy Imbalance Market (EIM) - 2020 Salt River Project
- Energy Imbalance Market (EIM) - 2020 Seattle City Light

Fall 2020

- Contingency Modeling Enhancements - Transmission
- Energy Storage and Distributed Energy Resources Phase 3B
- Dispatch Operating Target Tariff Clarifications
- Intertie Deviation Settlement
- Excess Behind the Meter Production
- Market Settlement Timeline Transformation (BOG Nov 2019)
- EIM Enhancements 2020
- **Import Bidding and Market Parameters, (A.K.A. Import Bid Cost Verification and FERC Order 831) – June 2020 BOG**
- Automated Dispatch System (ADS) User Interface (UI) Replacement

Release Plan Summary: 2020 - 2022

Spring 2021

- Energy Imbalance Market (EIM) 2021 - Public Service Company of New Mexico
- Energy Imbalance Market (EIM) 2021 - North-Western Energy
- Energy Imbalance Market (EIM) 2021 - Los Angeles Dept. of Water and Power
- Energy Imbalance Market (EIM) 2021 - Turlock Irrigation District
- Energy Imbalance Market (EIM) 2021 – BANC Ph 2/WAPA

Fall 2021 – tentative, subject to impact assessment

- Day Ahead Market Enhancements (BOG Q4 2020)
- RA Enhancements (BOG May/June 2020)
- Energy Storage and Distributed Energy Resources Phase 4 (BOG Q1 2020)
- Storage as a Transmission Facility (BOG TBD)
- TAC Structure Enhancements (Q4 - BOG)

Spring 2022

- Energy Imbalance Market (EIM) 2022 - Avista
- Energy Imbalance Market (EIM) 2022 - Tucson Electric Power
- Energy Imbalance Market (EIM) 2022 – Tacoma Power
- Energy Imbalance Market (EIM) 2022 – Bonneville Power Administration

Fall 2022 – tentative, subject to impact assessment


- Commitment Costs and Default Energy Bid Enhancements Phase 2

Release Schedule 2019

Date of Data Refresh: 11/1/2019



Legend	
Market Simulation	CA ISO Holiday
External Testing	Deployment Week



MAP Stage Environment Window

ESDER3A	ESDER3A (09/03-10/11)
ESDER3A - Market Sim	ESDER3A - Market Sim (09/03-10/11)
RMRC PME	RMRC PME (09/03-10/11)
RMRC PME - Market Sim	RMRC PME - Market Sim (09/03-10/11)
LMPME	LMPME (09/03-10/11)
LMPME - Market Sim	LMPME - Market Sim (09/03-10/11)
FERC841	FERC841 (09/03-10/11)
FERC841 - Market Sim	FERC841 - Market Sim (09/03-10/11)
RTM Neutrality Settlement	RTM Neutrality Settlement (09/03-10/11)
RTM Neutrality Settlement - Market Sim	RTM Neutrality Settlement - Market Sim (09/03-10/11)
EIM2019	EIM2019 (09/03-11/04)
EIM2019 - Market Sim	EIM2019 - Market Sim (09/03-11/04)
CCDEBE1	CCDEBE1 (09/03-11/26)
CCDEBE1 - Market Sim	CCDEBE1 - Market Sim (09/03-11/26)
EIM 2020 SRP & SCL	EIM 2020 SRP & SCL (12/03-01/31)
EIM 2020 SRP & SCL - Market Sim	EIM 2020 SRP & SCL - Market Sim (12/03-01/31)

Production Environment Window

FNM DB 2019Q3	FNM DB 2019Q3 (09/17-09/19)
ESDER3A - DRRS	ESDER3A - DRRS (11/06)
ESDER3A	ESDER3A (11/13)
RMRC PME Implementation	RMRC PME Implementation (11/13)
LMPME	LMPME (11/13)
EIM2019	EIM2019 (11/13)
FERC841	FERC841 (11/13)
RTM Neutrality Settlement Implementation (Effective Date 08/01/19)	RTM Neutrality Settlement Implementation (11/13)
FNM DB 2019M11	FNM DB 2019M11 (11/19-11/21)
CCDEBE1	CCDEBE1 (12/04)
RMRC PME Effective Date	RMRC PME Effective Date (01/01)

2019 Fall Release

Fall 2019 Release – Overview

	Board Approval	External BRS	Config. Guides	Technical Specifications	Mkt Sim Scenarios	Draft Tariff*	BPMs	External Training	Market Sim	Production Activation
Fall 2019 Release - Overview		04/01/19	05/17/19	05/17/19	05/17/19	07/14/19	08/26/19	08/26/19	09/03/19 – 10/11/19	11/13/19
CCDEBE1	03/22/18	09/03/19	N/A	05/17/19 CMRI 07/10/19 SIBR 10/24/19 CMRI	N/A	05/10/19	10/04/19	10/08/19	10/14/19 – 11/26/19	12/04/19
ESDER3A	09/05/18	07/18/19	05/17/19 07/08/19	05/16/19 MF, DRRS, MRI-S	06/19/19 v1.1	05/28/19	07/30/19	08/26/19	09/03/19 – 10/11/19	11/06/19 - DRRS 11/13/19
RMR-CPME	03/28/19	07/25/19	06/03/19 07/08/19	N/A	06/27/19 v1.0	04/03/19	08/26/19	08/30/19	09/03/19 – 10/11/19	11/13/19 Effective 01/01/20
LMPME	03/28/19	04/01/19	N/A	05/16/19 CMRI 06/28/19 MF	06/17/19 v1.1	04/16/19	09/05/19	08/29/19	09/03/19 – 10/11/19	11/13/19
EIM2019	N/A	08/12/19	05/17/19	05/17/19 CMRI 07/03/19 BSAP 07/19/19 OASIS	N/A	N/A	07/30/19	08/26/19 09/18/19	09/03/19 – 11/04/19	11/13/19
FERC841	N/A	06/20/19	06/03/19	N/A	N/A	N/A	8/30/09	N/A	09/03/19 – 10/11/19	11/13/19
RTM Neutrality Settlement	07/25/19	10/01/19	07/31/19	N/A	N/A	07/30/19	08/26/19	08/27/19	09/25/19 – 10/11/19	11/13/19 Effective 08/01/19

Implementation plan available on the Release page at <http://www.caiso.com/Documents/ImplementationPlan-Fall2019Release.pdf>

Notes:

Items in **BLUE** are complete

Items in **RED** indicate a new date which is later than the target date listed on the overview line..

Fall 2019 Release – System Interface Changes

MF

Project	Change Type	API Service Name & Major Version, Artifacts	Minor Version	RDT	MAP Stage	Production Activation	Technical Specifications
ESDER3A LMPME CCDEBE1	Modify	RetrieveGeneratorRDT_MFRDv4 RetrieveGeneratorRDT_MFRDv4_DocAttach	20191001		Sep 5, 2019	Oct 29, 2019	5.1
ESDER3A LMPME	Modify	SubmitGeneratorRDT_MFRDv4 SubmitGeneratorRDT_MFRDv4_DocAttach	20191001	GRDT v13.0	Sep 5, 2019	Oct 29, 2019	5.1

SIBR/BSAP

System	Project	Change Type	API Service Name & Major Version, Artifacts	MAP Stage	Production Activation	Technical Specifications
SIBR	CCDEBE1	Modify	RetrieveCleanBidSet_SIBRv5 RetrieveCleanBidSet_SIBRv5_DocAttach	Oct 16, 2019	Dec 4, 2019	13.1
SIBR	CCDEBE1	Modify	RetrieveCurrentBidResults_SIBRv5 RetrieveCurrentBidResults_SIBRv5_DocAttach	Oct 16, 2019	Dec 4, 2019	13.1
SIBR	CCDEBE1	Modify	SubmitRawBidSet_SIBRv5 SubmitRawBidSet_SIBRv5_DocAttach	Oct 16, 2019	Dec 4, 2019	13.1
BSAP	EIM 2019	Modify	RetrieveBalancingTestResults_BSAPv2 RetrieveBalancingTestResults_BSAPv2_DocAttach	Oct 16, 2019	Nov 13, 2019	1.7.1

Fall 2019 Release – System Interface Changes

CMRI

Project	Change Type	UI Change	API Service Name & Major Version, Artifacts	MAP Stage	Production Activation	Technical Specifications
LMPME CCDEBE1	Modify	Tab: Default Bids Existing Report: Default Energy Bid Curves	RetrieveDefaultBidCurves_CMRIv2 RetrieveDefaultBidCurves_CMRIv2_DocAttach	Sep 12, 2019	Nov 13, 2019	3.9.1
CCDEBE1	Modify	Tab: Default Bids Existing Report: Default Commitment Costs	RetrieveExternalDefaultCommitmentCost_CMRIv1 RetrieveExternalDefaultCommitmentCost_CMRIv1_DocAttach	Nov 6, 2019	Dec 4, 2019	3.9.1
EIM 2019	New	Tab: Energy Imbalance Market New Report: Resource Operating Limits	RetrieveEIMResourceOperatingLimit_CMRIv1 RetrieveEIMResourceOperatingLimit_CMRIv1_DocAttach	Oct 3, 2019	Nov 13, 2019	3.9.1
EIM 2019	New	Tab: Real-Time New Report: Resource Operating Limits	RetrieveResourceOperatingLimit_CMRIv1 RetrieveResourceOperatingLimit_CMRIv1_DocAttach	Oct 3, 2019	Nov 13, 2019	3.9.1

OASIS

Project	Change Type	UI Change	API Service Name & Major Version, Artifacts	MAP Stage	Production Activation	Technical Specifications
EIM 2019	New	Tab: ENERGY New Report: Transmission Loss	ENE_TRANS_LOSS	Oct 7, 2019	Nov 13, 2019	5.1.9

Fall 2019 – Commitment Cost and Default Energy Bid Enhancements Ph1

Project Info	Details/Date
Application Software Changes	<p><u>Scope:</u> Enhances the ability to submit market-based commitment cost bids in order to reflect unique costs and volatility:</p> <ul style="list-style-type: none"> • Ex-ante cost adjustment requests • Reference Level Adjustments to default commitment cost bids (start-up and minimum load costs) and default energy bids • Make Day Ahead Market process permanent • Make D+2 Process permanent • Use of indices clarification, and Monday Only in DAM and RTM, per LMPME • Conditionally Available Resources (CAR) <p><u>Impacted Systems:</u></p> <ul style="list-style-type: none"> • SIBR: Allow the submittal of Ex Ante cost adjustments. • CMRI: Provide additional source information for default bids. <p>Submit requests through CIDI for manual consultation and ex-post default bid adjustments.</p>
BPM Changes	<ul style="list-style-type: none"> • Market Instruments • Market Operations
Business Process Changes	<ul style="list-style-type: none"> • Maintain Major Maintenance Adders (MMG LIII) • Maintain Negotiated Default Energy Bids (MMG LIII) • Maintain Negotiated O_Ms (MMG LIII) • Manage Day Ahead Market (MMG LII) • Manage Market Billing Settlements (MOS LII) • Manage Real Time Hourly Market (RTPD) (MMG LII) • Manage Real Time Operations – Maintain Balance Area (MMG LII)

Fall 2019 – Commitment Cost and Default Energy Bid Enhancements Ph1

Milestone Type	Milestone Name	Dates	Status
Draft Policy	Publish Draft Business Rules externally	Jan 31, 2018	✓
Board Approval	Obtain Board of Governors Approval	Mar 22, 2018	✓
External BRS	Publish revised external BRS v1.1	Jan 22, 2019	✓
	Publish External BRS v1.2: Phase 1/Phase 2, clarifications	Mar 29, 2019	✓
	Publish External BRS v1.3: Reference Level Adjustments	Apr 05, 2019	✓
	Publish External BRS v1.4 for CCDEBE tariff traceability	Jul 19, 2019	✓
	Publish External BRS v1.5: implementation notes & clarifications (BRQ046, BRQ035/335), Generic Hub GPI update	Sep 04, 2019	✓
Config Guides	Config Guide	N/A	
Tech Spec	Publish Technical Specifications	May 17, 2019	✓
	Publish Technical Specification updates for CARs and Electric Pricing Hub weighting	Jun 28, 2019	✓
Tariff	File Tariff - CCDEBE Phase 1	Oct 11, 2019	✓
	Draft Tariff published	May 13, 2019	✓
	Tariff stakeholder walkthrough conference call	Jun 11, 2019	✓
BPMs	Publish draft Market Instruments: Attachment O on CCDEBE Stakeholder Processes page	Oct 04, 2019	✓
	PRR 1203 published: CCDEBE updates to Market Instruments BPM, incl. Attachment O	Oct 18, 2019	✓
External Training	Deliver External Training	Oct 08, 2019	✓
	Finalize external training material	Oct 04, 2019	✓
Market Sim	Market Sim Window	Oct 14, 2019 - Nov 26, 2019	
Production Activation	CCDEBE Phase 1	Dec 04, 2019	

* Project schedule shows risk in meeting current targets. Project team attempting to mitigate risk. Tariff filing requested a “no-later-than” Dec 11 effective date.

Fall 2019 – ESDER Phase 3a – Bid Dispatchable Option

Project Info	Details/Date
<p>Application Software Changes</p>	<p><u>Scope:</u> The ESDER 3a scope of the larger ESDER3 initiative will include two (2) demand response enhancements:</p> <ul style="list-style-type: none"> • New bid dispatchable options for demand response resources • Removal of single LSE requirement for PDR registrations & removal of default load adjustment (DLA) <p>Additionally, for ESDER2 Tariff Compliance, following is being implemented as part of this project</p> <ul style="list-style-type: none"> • Customer Load Baseline Submittal <p><u>Impacted Systems (Overview):</u></p> <p>Master File:</p> <ul style="list-style-type: none"> • RDTs for PDR registrations in MF will require selection of an effective Bid Dispatchable Option to be used for market optimization and dispatch <p>DRRS:</p> <ul style="list-style-type: none"> • PDR registrations will not require all service accounts to have the same LSE <p>SIBR:</p> <ul style="list-style-type: none"> • Will apply Net Benefit Test price criteria for PDR bids and reject those not meeting the applicable criteria • Will not allow Bid Dispatchable Options to be changed in SIBR <p>HASP/RTM:</p> <ul style="list-style-type: none"> • Will use effective Bid Dispatchable Option registered in MF (e.g., 5-min, 15-min or Hourly) for market optimization and dispatch instructions • Will broadcast new PDR energy schedules/awards and instructions to downstream applications <p>Settlements:</p> <ul style="list-style-type: none"> • Will remove the default load adjustment (DLA) application • Will provide Bid Cost Recovery for PDRs with 15-Minute Bids but not Hourly Bids <p>CMRI:</p> <ul style="list-style-type: none"> • Will include energy schedules and awards for PDRs with new Bid Dispatchable Options (Existing) <p>MRI-Settlements (ESDER2 Tariff Compliance):</p> <ul style="list-style-type: none"> • New BASE measurement type for monitoring calculated baseline data


Fall 2019 – ESDER Phase 3a – Bid Dispatchable Option (cont.)

Project Info	Details/Date
BPM Changes	<ul style="list-style-type: none"> Market Instruments, Metering, and Demand Response (new BPM) Market Operations
Tariff Change	4.13 and 11.6

Milestone Type	Milestone Name	Dates	Status
Board Approval	Obtain Board of Governors Approval	Sep 05, 2018	✓
External BRS	Post Revised External BRS v1.3	Jun 20, 2019	✓
	Post Revised External BRS v1.2	Mar 20, 2019	✓
	Post Revised External BRS v1.1	Feb 25, 2019	✓
	Post External BRS v1.0	Feb 11, 2019	✓
	Post Revised External BRS v1.4	Jul 18, 2019	✓
Config Guides	Post Draft Config Guides	May 17, 2019	✓
Tech Spec	Publish Technical Specifications	May 17, 2019	✓
Tariff	File Tariff	Sep 03, 2019	✓
BPMs	Post Draft BPM (DR, MI & Metering) changes	Jul 30, 2019	✓
	Post draft BPM changes - Market Operations	Aug 20, 2019	✓
External Training	External training	Aug 26, 2019	✓
Market Sim	ESDER 3a	Sep 03, 2019 - Oct 11, 2019	✓
Production Activation	ESDER 3a - DRRS	Nov 06, 2019	
	ESDER 3a - IFM/RTN, Settlements, SIBR	Nov 13, 2019	

Fall 2019 – ESDER Phase 3a – Bid Dispatchable Option (cont.)

Proposed DRRS & MF Transition Timeline

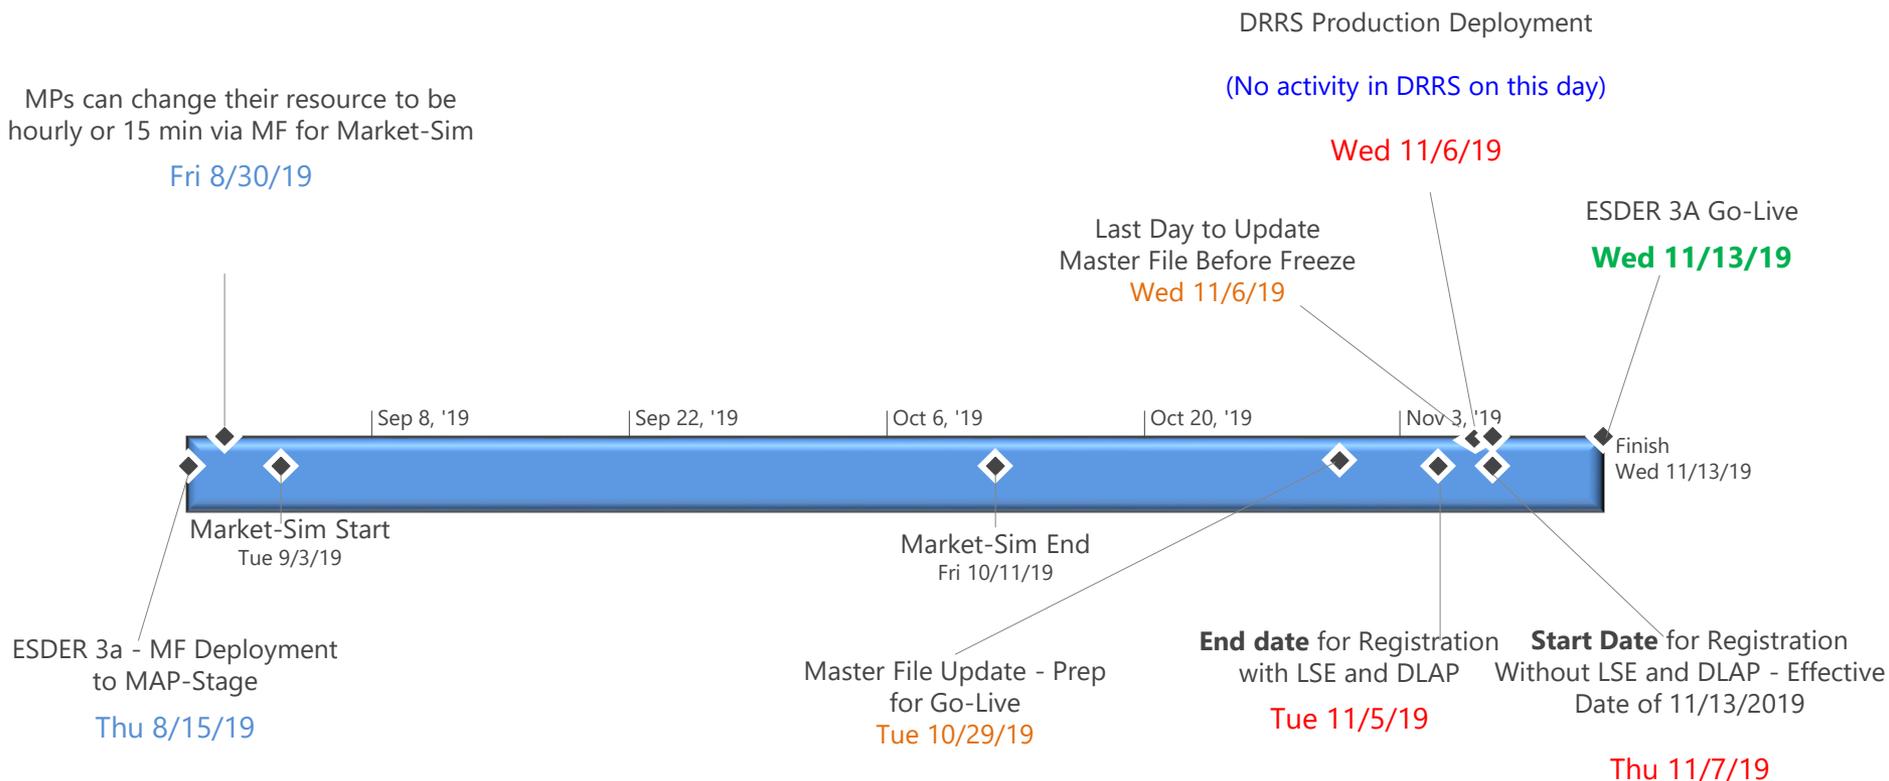

Fall 2019 – RMR and CPM Enhancements

Project Info	Details/Date
Application Software Changes	<p><u>Scope:</u> RMR and CPM Enhancements will address the following policy and tariff amendment scope:</p> <ul style="list-style-type: none"> • Risk-of-Retirement tariff provisions will transition from CPM to RMR section • RMR units under the new tariff provisions shall: <ul style="list-style-type: none"> Have reliability capacity allocated by TAC Area (for PTOs, not LSEs), Flex RA credit shall be applied Receive Must-Offer Obligation (MOO) Subject to RAAIM Streamline RMR invoicing, settlement process through inclusion in ISO Settlement process <p><u>Impacted Systems (Overview):</u></p> <p>Master File:</p> <ul style="list-style-type: none"> • No impact. ISO will internally manage RMR resource status and vintage (e.g. RMR vs. RMRL). <p>CIRA:</p> <ul style="list-style-type: none"> • New features to both qualify (e.g. confirm EFC is defined) and allocate System/Local/Flex reliability capacity by TAC Area (for PTOs) for RMR units with new contract type: <ul style="list-style-type: none"> • Apply Flex RA credit by TAC Area (for PTOs) • Perform RMR Substitution • Support RMR Risk-of-Retirement • Like RA resources, RMR units under the new tariff will receive RAAIM status determination <p>SIBR</p> <ul style="list-style-type: none"> • Like RA resources, automatically generates cost-based energy bids for new contract type RMR units for un-submitted bid range below RMR contract capacity <ul style="list-style-type: none"> • Bids will reflect applicable GHG Compliance costs, SC charges, Major Maintenance Adder (MMA), and (if applicable) Opportunity Costs (OC); Note: MMA and OC are recovered through fixed cost payments (not market rents) and will be clawed-back during the ISO settlement process. • Removes self-schedule requirement for new contract type RMR units scheduled/dispatched in Day-Ahead Market <p>IFM/RTM:</p> <ul style="list-style-type: none"> • Unit Commitment, Economic Dispatch decisions will include applicable MMA and OC (no change from today) • Like RA resources, new contract type RMR units will have automatic RA Obligation (\$0/MWh bids in RUC)

Fall 2019 – RMR and CPM Enhancements (cont.)

Project Info	Details/Date
Application Software Changes	<p><u>Impacted Systems (Continued):</u></p> <p>IFM/RTM:</p> <ul style="list-style-type: none"> • Unit Commitment, Economic Dispatch decisions will include applicable MMA and OC (no change from today) • Like RA resources, new contract type RMR units will have automatic RA Obligation (\$0/MWh bids in RUC) <p>Settlements:</p> <ul style="list-style-type: none"> • RMR units under new contract type will receive: <ul style="list-style-type: none"> • RMR under new tariff provisions will settle through the ISO Settlements calendar; • Legacy RMR (RMRL) will continue to receive payment through the RMR invoicing process • Monthly RMR capacity payment (by resource) and cost allocation (by PTO) • RAAIM settlement/allocation • Bid Cost Recovery (does not include MMA or OC) • Clawback of fixed MMA and OC costs (if applicable) <p>CPM tariff revisions will be addressed during the CPM Soft Offer Cap policy initiative.</p>
BPM Changes	Reliability Requirements, Generator Management, Market Operations, Market Instruments, Settlements and Billing
Tariff Change	11.13, 31.2.2, 34.1, 40.9, 41, 43, 43A, Appendix G

Fall 2019 – RMR and CPM Enhancements (cont.)

Milestone Type	Milestone Name	Dates	Status
Board Approval	Board of Governors Approval	Mar 28, 2019	✓
External BRS	Post External BRS	Apr 01, 2019	✓
	Post Updated External BRS v1.1	Jul 26, 2019	✓
Config Guides	Publish Config Guide	Jun 03, 2019	✓
Tech Spec	Publish Technical Specifications	N/A	
Tariff	Receive FERC order (Approval)	Sep 27, 2019	✓
	File Tariff w/ FERC	Apr 23, 2019	✓
	Receive FERC order (Deficiency Letter)	Jul 19, 2019	✓
	Refiled with FERC	Jul 26, 2019	✓
BPMs	Post Draft BPM changes	Oct 31, 2019	✓
External Training	Deliver External Training	Aug 30, 2019	✓
Market Sim	RMR/CPM	Sep 03, 2019 - Oct 11, 2019	✓
Production Activation	RMR/CPM Deployment	Nov 13, 2019	
	RMR/CPM Effective Date	Jan 01, 2020	

Fall 2019 – Local Market Power Mitigation Enhancements

Project Info	Details/Date
Application Software Changes	<p>Scope Prevent flow reversal, DEB for Hydro, Reference level adjustment process, Gas price Indices</p> <p>Impacted Systems</p> <p>RTM: Prevent flow reversal Eliminate rule mitigate in FMM carry to RTD Eliminate rule mitigate for balance of hour for FMM, balance 15 minute for RTD Use current market competitive LMP for mitigation Add a nominal parameter to mitigated bids Mitigated bid = MAX (DEB, Competitive LMP + \$0.xx parameter)</p> <p>CMRI: Display new Hydro DEB type</p> <p>Master File: Manage Hydro DEB eligibility at resource level New field to select and rank hydro DEB option Store resource's maximum storage horizon Identify default trading hubs for hydro resources, requests changes to additional hubs Ability to view parameters and ranking of approved hydro DEBs</p>
BPM Changes	Market Operations, Market Instruments
Tariff Change	Section 29.39, 31.2.1, 39.7

Fall 2019 – Local Market Power Mitigation Enhancements (cont.)

Milestone Type	Milestone Name	Dates	Status
Board Approval	Board of Governors Approval	Mar 28, 2019	✓
External BRS	Post External BRS	Apr 01, 2019	✓
Config Guides	Post Draft Config Guides	N/A	
Tech Spec	Publish Technical Specifications: MF v5.0, CMRI v3.9.0	May 17, 2019	✓
	Publish Technical Specification update: CARs, Electric Pricing Hub weighting, MF v5.1	Jun 28, 2019	✓
Tariff	File Tariff	Jul 02, 2019	✓
BPMs	Post Draft BPM changes: PRRs 1190 (MI), 1191 (MO), 1192 (EIM)	Sep 05, 2019	✓
External Training	Deliver External Training	Aug 29, 2019	✓
Market Sim	Market Sim Window	Sep 03, 2019 - Oct 11, 2019	✓
Production Activation	LMPM - Enhancements	Nov 13, 2019	

Fall 2019 – Energy Imbalance Market Enhancements 2019

Project Info	Details/Date
Application Software Changes	<p>Scope: Implement 21 EIM enhancements requested by EIM entities through CIDI System</p> <p>Impacted Systems: BAAOP: Add displays for BAA overview, Unit deviations, Load Bias, transfer limits, contingency flag, timestamps, and other identified items. Enhance sorting and layouts ability. Enhance alarm ability for market thresholds. BSAP: Enhance capability for Base schedule modification, Add aggregated BS deviation in API. OASIS or CMRI: Display ROC limits Display 5-min market transmission Loss RTM: prevent ETSR swing using explicit triggers. ADS: Publish current DOP in the MSG transition period. Settlement: Publish data for UFE shadow calculation; Settle EIM Resource Deviation within Regulation/ABC range as instructed regulation energy. CMRI: Publish resource limit values</p>
BPM Changes	Market Instruments, Energy Imbalance Market

Milestone Type	Milestone Name	Dates	Status
Board Approval	Obtain Board of Governors Approval	N/A	
External BRS	Milestone: Post External BRS	Feb 05, 2019	✓
	Milestone: Post External BRS Revisions 1.1	Mar 25, 2019	✓
	Milestone: Post External BRS Revisions 1.4	Aug 12, 2019	✓
Config Guides	Publish Config Guides	May 17, 2019	✓
Tech Spec	ISO Interface Spec (Tech spec) – BSAP v1.6, CMRI v3.9.0	May 17, 2019	✓
	Create ISO Interface Spec (Tech spec) – OASIS v5.1.9	Jul 19, 2019	✓
	Revised ISO Interface Spec (Tech spec) – BSAP v1.7	Jul 03, 2019	✓
Tariff	File Tariff	N/A	
BPMs	Post Draft BPM changes	Jul 30, 2019	✓
External Training	External Training Webinar	Aug 26, 2019	✓
	External Training Webinar/Refresh (During Bi-Weekly Ops Call)	Sep 18, 2019	✓
Market Sim	Market Sim Window	Sep 03, 2019 - Nov 04, 2019	
Production Activation	EIM Enhancements 2019	Nov 13, 2019	

Fall 2019 – FERC 841 Energy Storage Resources

Project Info	Details/Date
Application Software Changes	<p>Scope: FERC issued Order 841 to remove the barriers to the participation of electric storage resources in the capacity, energy and ancillary service markets operated by RTOs and ISOs.</p> <p>CAISO will achieve compliance with Order 841 through implementation of two (2) specific scope items:</p> <ul style="list-style-type: none"> • Reduce the minimum capacity for participating Generators to 100kW for storage resources • Remove Transmission Access Charge (TAC) for Pumped-Storage Hydro Units
BPM Changes	Market Operations, Settlements and Billing
Tariff Change	<p>4.6.3.2 – Exemption for Generating Units of Less Than One (1) MW</p> <p>26.1 – Transmission Rates and Charges</p> <p>Appendix A – Definition Change for Participating Generator</p>

Milestone Type	Milestone Name	Dates	Status
Board Approval	Obtain Board of Governors Approval	N/A	
External BRS	Milestone: Post External BRS	Jun 20, 2019	✓
Config Guides	Milestone: Post Config Guide	Jun 03, 2019	✓
Tech Spec	N/A: Publish Technical Specifications	Aug 13, 2019	✓
Tariff	CAISO's Compliance Filing	Dec 8, 2018	
BPMs	Settlements & Billing – PRR #1177 released	Aug 26, 2019	✓
	Market Operations – PRR #1180 released	Aug 30, 2019	✓
	Generator Management – PRR align with Tariff effective date	Align with Tariff effective date	
External Training	External training	N/A	
Market Simulation	Market Sim Environment Window - Phase 1	Sep 03, 2019 - Oct 11, 2019	✓
Production Activation	FERC 841 - NGR Model	Nov 13, 2019	

Fall 2019 – Real-Time Market Neutrality Settlement

Project Info	Details/Date
Application Software Changes	Settlement: modify CC6477, CC64770 <ul style="list-style-type: none"> Remove EIM transfer adjustment amount Credit the GHG cost for non-CA transfers in EIM transfer financial value calculation Use 5-minute ETSR After-The-Fact tags submitted by EIM BAA
BPM Changes	Settlements & Billing
Tariff Change	11.5.4.1 Real Time Imbalance Energy Offset

Milestone Type	Milestone Name	Dates	Status
Board Approval	Obtain Board of Governors Approval	Jul 25, 2019	✓
External BRS	Post External BRS	Jul 08, 2019	✓
	Post External BRS (Updated)	Aug 07, 2019	✓
Config Guides	Publish Config Guide	Jul 31, 2019	✓
Tech Spec	Publish Technical Specifications	N/A	
Tariff	File Tariff w/FERC	Jul 30, 2019	✓
BPMs	Post Draft BPM changes	Aug 26, 2019	✓
External Training	Deliver External Training	Aug 27, 2019	✓
Market Sim	Market Sim Window	Sep 03, 2019 - Oct 11, 2019	✓
Production Activation	RT Market Neutrality Settlement	Nov 13, 2019	

2020 Spring Release

Spring 2020 – EIM integrations for SCL and SRP

Project Info	Details/Date
Application Software Changes	Implementation of SCL and SRP as EIM Entities
BPM Changes	EIM BPM will be updated if needed to reflect new modeling scenarios identified during implementation and feedback from SCL and SRP.
Market Simulation	December 2019 – January 2020
Parallel Operations	February 2020 – March 2020

Milestone Type	Milestone Name	Dates	Status
Market Sim	Market Sim Window	December 2019 – January 2020	
Parallel Operations	Parallel Operations	February 2020 – March 2020	
Tariff	File Readiness Certification	March 2020	
Production Activation	EIM – SCL and SRP	April 2020	

2020 Fall Release

Fall 2020 Release – Overview

	External BRS	Config Guide	Tech Spec	Mkt Sim Scenarios	Draft Tariff*	BPMs	External Training	Market Sim	Production Activation
Fall 2020 Release	04/01/20	05/29/20	05/29/20	05/29/20	06/26/20	07/20/20	07/20/20	Jul 7, 2020 – Sep 4, 2020	10/01/20
Contingency Modeling Enhancements - Transmission								Jul 7, 2020 – Sep 4, 2020	10/01/20
ESDER Phase 3b - Load Shift Product	07/18/19	02/20/20	03/13/20		3/30/20	05/27/20	06/22/20	Jul 7, 2020 – Sep 4, 2020	10/01/20
Dispatch Operating Target Tariff Clarification	12/26/18							Jul 7, 2020 – Sep 4, 2020	10/01/20
Intertie Deviation Settlement								Jul 7, 2020 – Sep 4, 2020	10/01/20
Excess Behind the Meter Production								Jul 7, 2020 – Sep 4, 2020	10/01/20
Market Settlement Timeline Transformation								Jul 7, 2020 – Sep 4, 2020	10/01/20
EIM Enhancements 2020								Jul 7, 2020 – Sep 4, 2020	10/01/20
Import Bidding and Market Parameters								Jul 7, 2020 – Sep 4, 2020	10/01/20
ADS UI Replacement								Jul 7, 2020 – Sep 4, 2020	10/01/20

Fall 2020 – ESDER Phase 3b – Load Shift Product

Project Info	Details/Date
Application Software Changes	<p><u>Scope:</u></p> <p>The ESDER 3b initiative will include two (2) demand response enhancements:</p> <ul style="list-style-type: none">• Addition of a Load Shift Product wherein demand response resources with behind the meter (BTM) storage devices can participate in both load consumption and load curtailment.• Enable sub-metered electric vehicles supply equipment (EVSE) to participate in load curtailment <p><u>Impacted Systems (Overview):</u></p> <p>Master File:</p> <ul style="list-style-type: none">• Registration of new PDR Resource Types and business rules for PDRs with BTM storage devices and wanting to participate in both Load Curtailment and Consumption• Two (2) Resource IDs will be assigned to the same Resource to allow Consumption versus Curtailment participation (PDR-LSR) <p>DRRS:</p> <ul style="list-style-type: none">• Allow two resource IDs to be selected for registrations with LSR baseline methods• New baseline methods for PDR-LSRs and EVSEs• New attribute for locations to indicate BTM device <p>CIRA:</p> <ul style="list-style-type: none">• Will prevent the request of NQC for PDR-LSR Consumption resources

Fall 2020 – ESDER Phase 3b – Load Shift Product (cont.)

Project Info	Details/Date
BPM Changes	<ul style="list-style-type: none"> Market Instruments, Market Operations, Outage Management, Reliability Requirement and Metering
Tariff Change	Sections 4.13, 6.4, 6.5, 11.6, 11.8, 31.3, 34.1,34.4, 34.5, 30.7 and 34.8

Milestone Type	Milestone Name	Dates	Status
Board Approval	Obtain Board of Governors Approval	Sep 05, 2018	✓
External BRS	Post External BRS v1.4	Jul 18, 2019	✓
Config Guides	Post Draft Config Guides	Feb 20, 2020	
Tech Spec	Publish Technical Specifications	Feb 25, 2020	
Tariff	Post Draft Tariff	Mar 30, 2020	
	File Tariff	Jun 11, 2020	
BPMs	Post Draft BPM changes	May 27, 2020	
External Training	External training	Jun 22, 2020	
Market Sim	Market Sim Window	Jul 7, 2020 – Sep 4, 2020	
Production Activation	ESDER Phase 3b - Load Shift Product	Oct 01, 2020	

Fall 2020 – Dispatch Operating Target Tariff Clarification

Project Info	Details/Date
Application Software Changes	<p>Scope: Allow Energy Intermittent Resources (EIRs) to automate their response to operational instructions that require the resource not to exceed their Dispatch Operating Target.</p> <p>Impacted Systems: RTM: Operator can select EIR resources, system to send Operating instruction Flag to ADS ADS: Receive Operating instruction flag for EIRs. Broadcast message to EIRs operator.</p>
BPM Changes	Market Instruments Market Operations
Tariff Change	Changes tariff language from “Operating Order” to “Operating Instruction” in multiple sections.

Milestone Type	Milestone Name	Dates	Status
Board Approval	Obtain Board of Governors Approval	Jul 26, 2018	✓
External BRS	Milestone: Post External BRS	Dec 26, 2018	✓
Config Guides	Design review - BPM and Tariff SMEs	N/A	
Tech Spec	Create ISO Interface Spec (Tech spec)	TBD	
Tariff	Draft Tariff	Sep 04, 2018	✓
	File Tariff	Oct 29, 2018	✓
BPMs	Publish Final Business Practice Manuals	Jul 20, 2020	
External Training	Deliver External Training	Jul 20, 2020	
Market Sim	Market Sim Window	Jul 07, 2020 - Sep 04, 2020	
Production Activation	Dispatch Operating Target Tariff Clarification	Oct 01, 2020	

Fall 2020 – Intertie Deviation Settlement

Project Info	Details/Date
Application Software Changes	<p>Scope: Implement a new Under/Over Delivery Charge for intertie deviations from Market Schedule and After-The-Fact (ATF) E-Tag, to replace Decline charge</p> <p>Impacted Systems: Settlements</p> <ul style="list-style-type: none">• Calculate FMM binding intertie award, exclude Curtailment, calculate under/over delivery quantity as deviation of schedule and ATF E-Tag, Charge under/over delivery Charge at 50% of RTD LMP.• Remove the decline charge calculation and Decline Threshold• Allocate Over/Under delivery charge to measured demand
BPM Changes	Settlements and Billing
Tariff Change	Section 11.31

Fall 2020 – ADS Replacement

Project Info	Details/Date
Application Software Changes	<ul style="list-style-type: none"> • Transition to web-based user interface to eliminate the need to install thick client • Transition ADS provisioning to the Access and Identity Management (AIM) application including Resource Level Access Controls (RACL) access • The query tool will provide 30 days of historical data • Various user interface enhancements adding content per Operation's request • ADS B2B services changes - TBD.
BPM Changes	<ul style="list-style-type: none"> • Market Instruments • Market Operations

Milestone Type	Milestone Name	Dates	Status
Board Approval	Obtain Board of Governors Approval	N/A	
External BRS	Post External BRS	Aug 06, 2018	✓
ADS Update	ADS Update Meeting	Aug 15, 2018	✓
Config Guides	Design review - BPM and Tariff SMEs	N/A	
Tech Spec	Publish Technical Specifications	N/A	
Tariff	File Tariff	N/A	
BPMs	Post Draft BPM changes	TBD	
Market Sim	Market Sim Window	Q4 2020	
Production Activation	ADS Replacement	Q4 2020	
Production	ADS Parallel Operations	Q4 2020	
Decommission	Old ADS Decommission	TBD	

2021 Spring Release

Spring 2021 – EIM integrations for PNM, LADWP, TID, NWE and BANC Phase 2

Project Info	Details/Date
Application Software Changes	Implementation of PNM, LADWP, TID, NWE and BANC Phase 2 as EIM Entities
BPM Changes	EIM BPM will be updated if needed to reflect new modeling scenarios identified during implementation and feedback from PNM, LADWP, TID, NWE and BANC Phase 2.
Market Simulation	December 2020 – January 2021
Parallel Operations	February 2021 – March 2021

Milestone Type	Milestone Name	Dates	Status
Market Sim	Market Sim Window	December 2020 – January 2021	
Parallel Operations	Parallel Operations	February 2021 – March 2021	
Tariff	File Readiness Certification	March 2021	
Production Activation	EIM – PNM, LADWP, TID, NWE and BANC Phase 2	April 2021	

Stay Informed

Ways to participate in releases

- Visit the Release Planning page
 - <http://www.caiso.com/informed/Pages/ReleasePlanning/Default.aspx>
- Attend meetings
 - Release Users Group (RUG) bi-weekly meetings
 - Initiative status updates
 - System change updates on independent releases
 - Market Simulation calls
 - Visit the ISO calendar at www.caiso.com for meeting dates and times and add events to your calendar
 - Typically held on Mondays and Thursdays
 - Market Performance and Planning Forum
 - Bi-monthly review of market performance issues
 - High level discussion of release planning, implementation and new market enhancements

What to look for on the calendar...

Calendar of Meetings, Training and Events

Month: February Year: 2018 Calendar View List View Print View

February 2018						
Sun	Mon	Tue	Wed	Thu	Fri	Sat
	5	6	7	8	9	10
	<p>Market Sim →</p> <p>WebCONF: Market Simulation 2:00pm - 3:00pm</p>	<p>Training: Get to Know the ISO - Day 1 9:00am - 4:00pm</p> <p>WebCONF: Imbalance Conformance Enhancements 10:00am - 12:00pm</p> <p>WebCONF: Technical User Group 10:00am - 11:00am</p>	<p>Deadline: Comments - Interconnection Process Enhancements 2018 - Issue Paper and Meeting Discussion 9:00am - 4:00pm</p> <p>Training: Get to Know the ISO - Day 2 9:00am - 4:00pm</p> <p>Meeting: Flexible Resource Adequacy Criteria Must Offer Obligation Phase 2 - Revised Draft Flexible Capacity Framework 10:00am - 4:00pm</p> <p>WebCONF: Market Settlement User Group 10:00am - 11:00am</p>	<p>Meeting: Audit Committee Teleconference (Executive) 8:30am - 9:30am</p> <p>Training: Settlements 101 9:00am - 4:00pm</p> <p>Meeting: 2017-2018 Transmission Planning Process 10:00am - 4:00pm</p> <p>Market Sim ←</p> <p>WebCONF: Market Simulation 2:00pm - 3:00pm</p>	<p>Training: Settlements 201 9:00am - 4:00pm</p>	
11	12	13	14	15	16	17
<p>WebCONF: Participating Transmission Owner Per Unit Cost Guides 10:30am - 12:00pm</p> <p>WebCONF: Market Simulation 2:00pm - 3:00pm</p>	<p>Meeting: Congestion Revenue Rights Auction Efficiency 10:00am - 4:00pm</p> <p>WebCONF: Release User Group 10:00am - 11:00am</p> <p>Call: Energy Imbalance Market Governing Body Teleconference (Executive) 11:30am - 12:30pm</p>	<p>Deadline: Submissions - April 2018 Monthly Resource Adequacy and Supply Plans 11:00am - 11:30am</p> <p>Call: Congestion Revenue Rights 11:00am - 11:30am</p> <p>WebCONF: Outage Management System Customer Partnership Group 2:00pm - 3:00pm</p>	<p>Deadline: Comments - Review Transmission Access Charge Structure Straw Proposal and Meeting Discussion 11:00am - 11:30am</p> <p>Call: Board of Governors Teleconference (General) 8:15am - 9:00am</p> <p>Call: Board of Governors Teleconference (Executive) 9:00am - 10:00am</p> <p>Call: Market Update 10:15am - 11:00am</p> <p>WebCONF: Market Simulation</p>			

Release Users Group (RUG) →
